ID	Task Name	Duration	Start	Finish
1	Mobilization	7 days?	04 Aug '09	12 Aug '09
2	Potholing	4 days?	05 Aug '09	10 Aug '09
3	Tree Protection	6 days?	05 Aug '09	12 Aug '09
4	Erosion Control	3 days?	05 Aug '09	08 Aug '09
5	Temporary Fencing	4 days?	06 Aug '09	11 Aug '09
6	Creek Diversion	2 days?	06 Aug '09	07 Aug '09
7	Inline Valve- Water line	4 days?	06 Aug '09	11 Aug '09
8	Removals	18 days?	05 Aug '09	28 Aug '09
9	Sanitary Sewer Work	7 days?	10 Aug '09	18 Aug '09
10	Saddle Inlet at OSP	2 days?	11 Aug '09	12 Aug '09
11	Trash Structure	31 days?	12 Aug '09	23 Sep '09
12	Fencing at Trash Structure	5 days?	14 Sep '09	18 Sep '09
13	Cobble at Trash Structure	2 days?	24 Sep '09	25 Sep '09
14	78" Storm Sewer	17 days?	13 Aug '09	05 Sep '09
15	48" Storm Sewer	17 days?	13 Aug '09	05 Sep '09
16	Irrigation Meter Pit at Roundabout	4 days?	17 Aug '09	20 Aug '09
17	Irrigation System @ Roundabout	22 days?	20 Aug '09	18 Sep '09
18	Landscaping at roundabout	10 days?	21 Sep '09	02 Oct '09
19	Diversion Structure	20 days?	24 Aug '09	18 Sep '09
20	Guard Rail Installation	8 days?	21 Sep '09	30 Sep '09
21	18" Storm Sewer	13 days?	24 Aug '09	09 Sep '09
22	6" Storm Sewer	10 days?	26 Aug '09	08 Sep '09
23	Fire Hydrant	5 days?	31 Aug '09	04 Sep '09
24	2" Irrigation Service Line	5 days?	31 Aug '09	04 Sep '09
25	Gas Lines	8 days?	31 Aug '09	09 Sep '09
26	Electrical conduit	8 days?	31 Aug '09	09 Sep '09
27	Irrigation Sleeves	8 days?	31 Aug '09	09 Sep '09
28	SnowMelt Main Lines	10 days?	31 Aug '09	11 Sep '09
29	Irrigation Meter Pit at Plaza	8 days?	31 Aug '09	09 Sep '09
30	Light Pole Bases	8 days?	07 Sep '09	16 Sep '09
31	Trench Drain Lines	4 days?	07 Sep '09	10 Sep '09
32	Slopeside Fence Structure	10 days?	14 Sep '09	25 Sep '09
33	Colored concrete Bands/ V-Pan	13 days?	14 Sep '09	30 Sep '09
34	Asphalt Patching	2 days?	01 Oct '09	02 Oct '09
35	Granit Boulder Placement	5 days?	14 Sep '09	18 Sep '09
36	Stone Terrace	10 days?	14 Sep '09	25 Sep '09
37	Fire Pit Installation	11 days?	16 Sep '09	30 Sep '09
38	Stone Outcrop	11 days?	16 Sep '09	30 Sep '09
39	Seat Wall Drainage	3 days?	16 Sep '09	18 Sep '09
40	Stone Terrace Footer	2 days?	17 Sep '09	18 Sep '09
41	Concrete Seat Wall Lights	5 days?	17 Sep '09	23 Sep '09
42	Stone Veneer	4 days?	17 Sep '09	22 Sep '09
43	Stone Seat Walls	5 days?	21 Sep '09	25 Sep '09
44	Trench Grate Drain- Concrete	3 days?	23 Sep '09	25 Sep '09
45	Subgrade Prep	7 days?	01 Oct '09	09 Oct '09
46	9" Concrete Subgrade	5 days?	07 Oct '09	13 Oct '09
47	Electrical System	25 days?	12 Oct '09	13 Nov '09
48	Topsoil Placement	10 days?	12 Oct '09	23 Oct '09
49	Snowmelt tubing	11 days?	14 Oct '09	28 Oct '09
50	Colored Concrete Flatwork	10 days?	15 Oct '09	28 Oct '09
51	Irrigation System @ Plaza	10 days?	19 Oct '09	30 Oct '09
52	Landscape Drains	5 days?	19 Oct '09	23 Oct '09
53	Install Conrete Unit Pavers	15 days?	22 Oct '09	11 Nov '09
54	Landscaping @ Plaza	12 days?	28 Oct '09	12 Nov '09
55	Light Pole Installation	4 days?	09 Nov '09	12 Nov '09
56	Cleanup	9 days?	10 Nov '09	20 Nov '09
57	De-Mobilization	8 days?	16 Nov '09	25 Nov '09

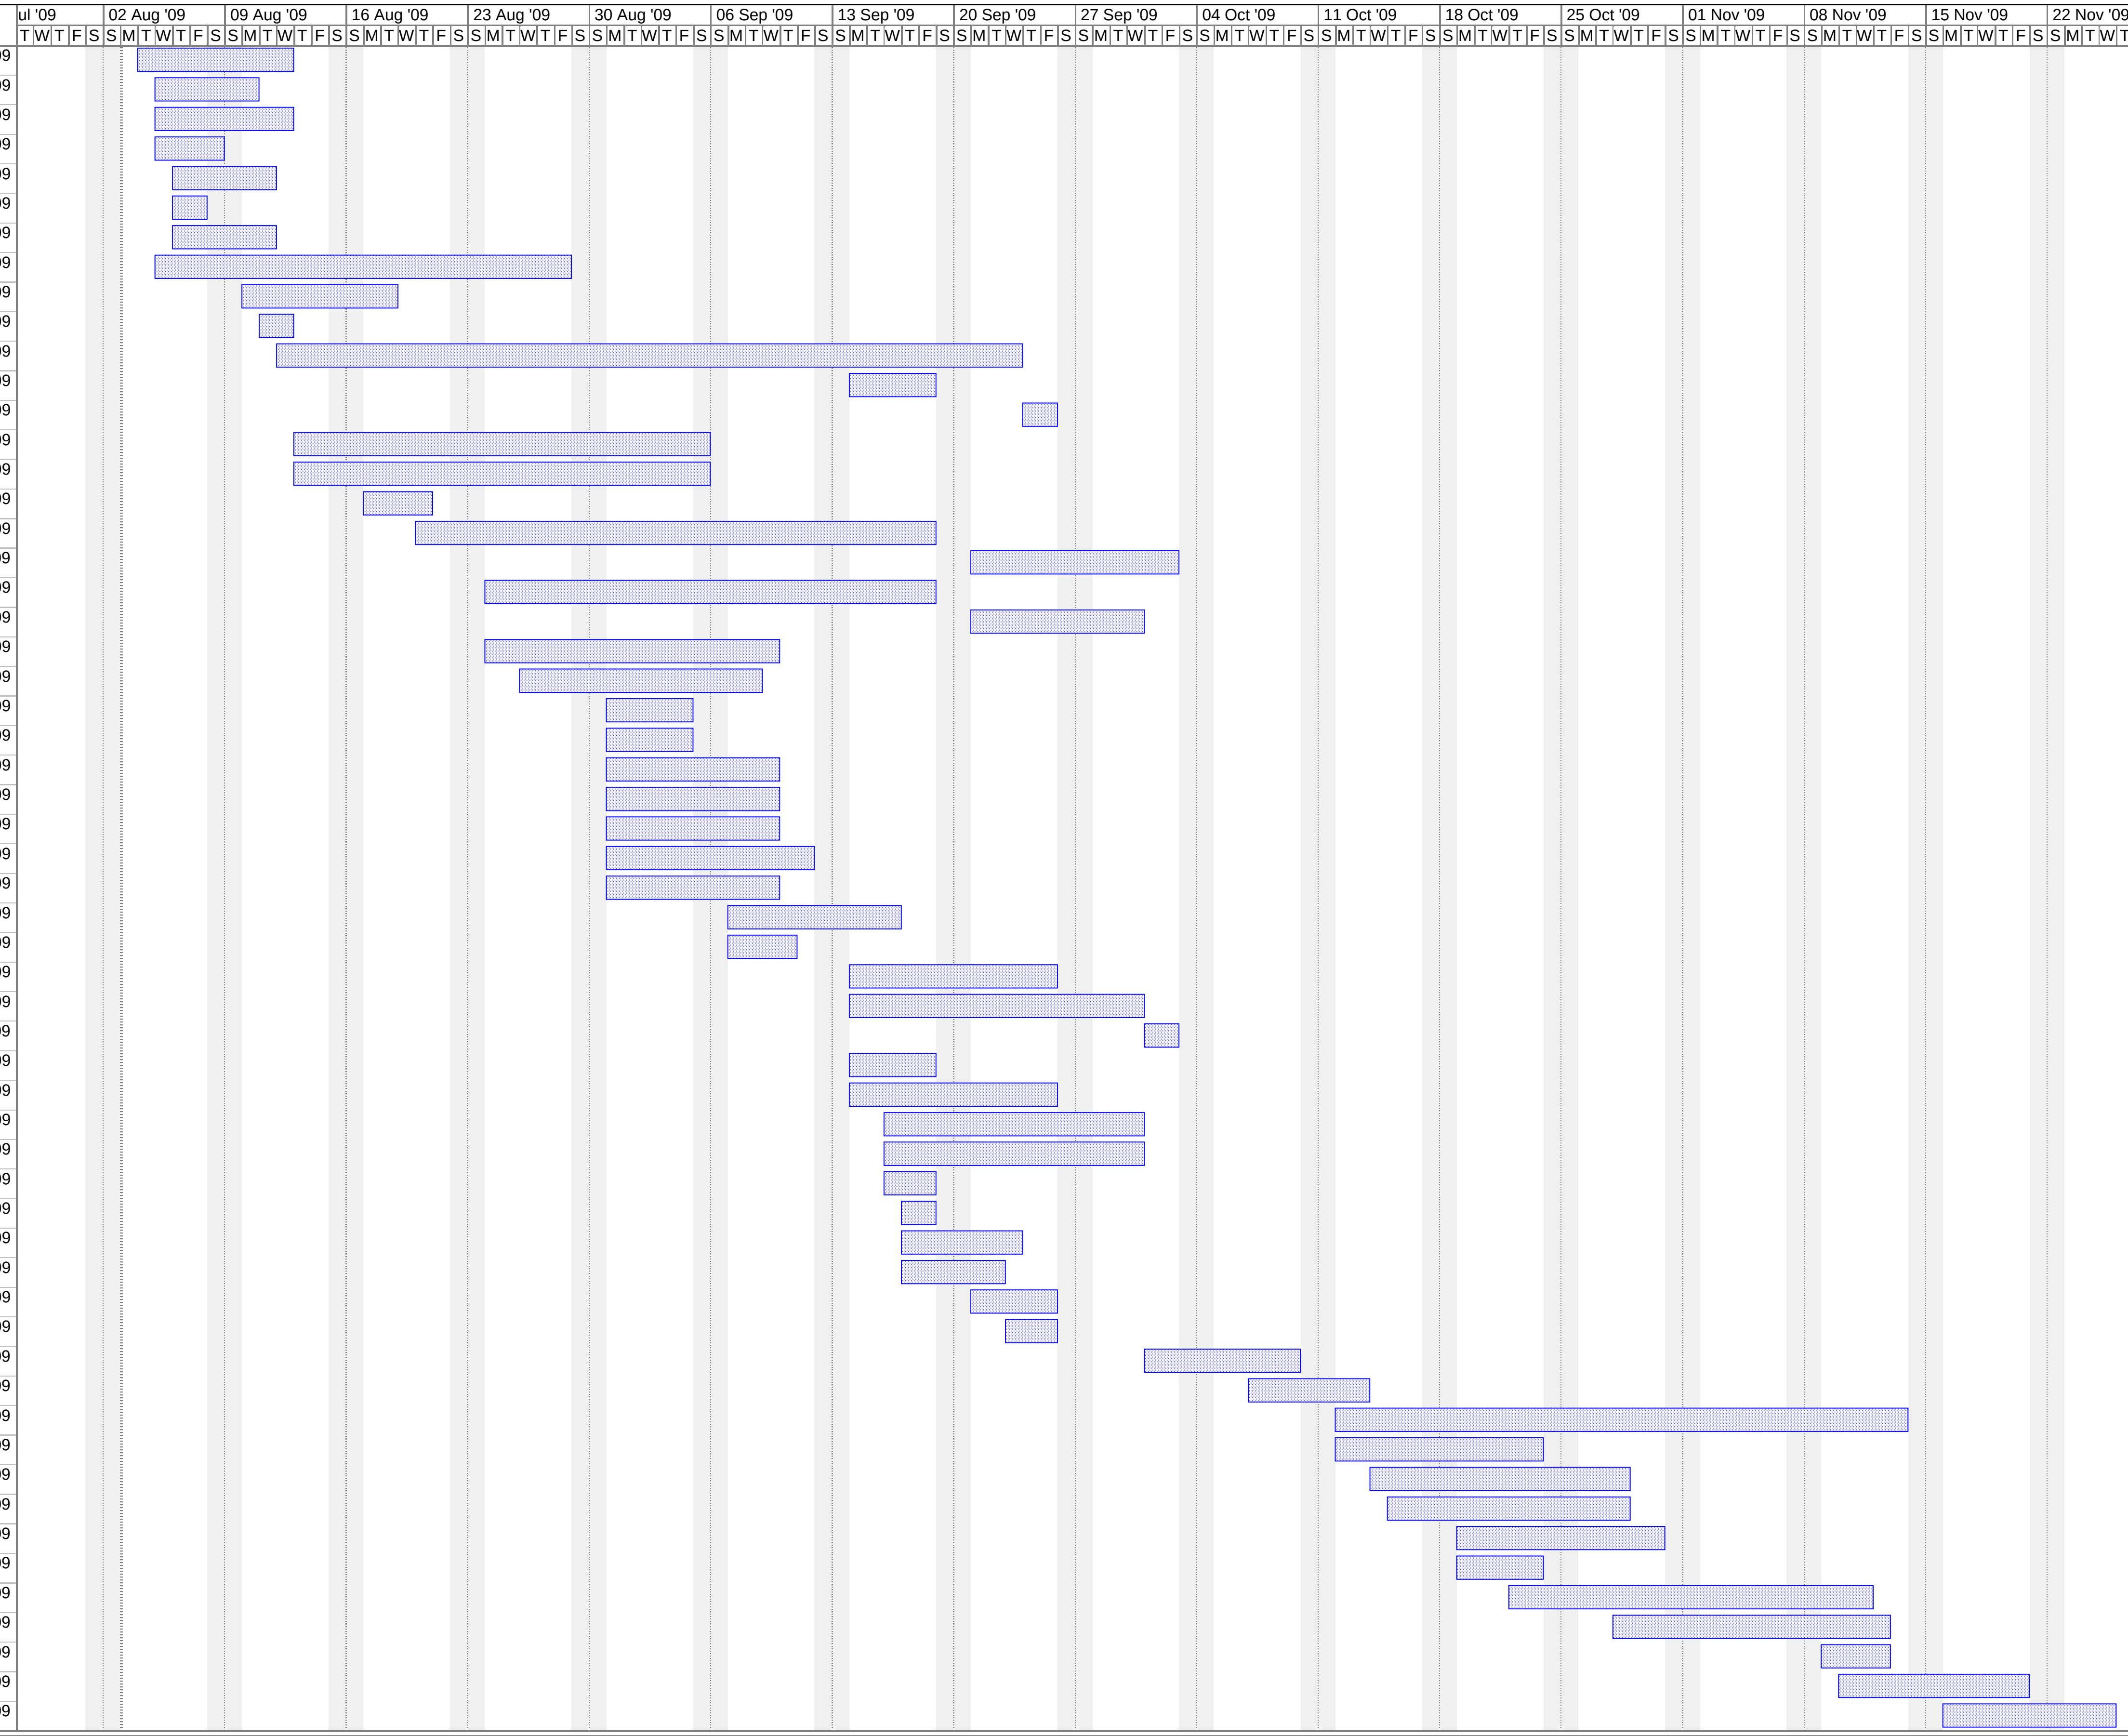

Project: Preliminary Schedule 1
Date: 03 Aug '09

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
